


ID	Task Name	Duration	Start	Finish	Resource Names	Jan '17	10	17	24	Jan '18
1	install cyclone fence at retaining wall	1 day	Tue 3/27/18	Tue 3/27/18	Quality Fence	3				31
2	complete underground work at State St intersection	5 days	Mon 3/26/18	Fri 3/30/18	Cradar					
3	trench patch State St intersection	1 day	Mon 4/2/18	Mon 4/2/18	Guido					
4	remove sidewalk portions from Umpqua to State St, north	5 days	Mon 3/26/18	Fri 3/30/18	Guido					
5	install conduit from Umpqua to State, north	2 days	Mon 4/2/18	Tue 4/3/18	Kunert					
6	set curb and sidewalk forms, place tree grates for State to Umpqua	4 days	Thu 3/29/18	Tue 4/3/18	Guido					
7	pour curb and sidewalk from State to Umpqua, north	2 days	Wed 4/4/18	Thu 4/5/18	Guido					
8	set root barriers and place topsoil from State to Umpqua	2 days	Fri 4/6/18	Mon 4/9/18	Guido					
9	trench patch from State to Umpqua, north	1 day	Fri 4/6/18	Fri 4/6/18	Guido					
10	begin underground work at Calapooia intersection	8 days	Tue 4/3/18	Thu 4/12/18	Cradar					
11	begin demo of curb and sidewalk from State to Calapooia, north	5 days	Mon 4/9/18	Fri 4/13/18	Guido					
12	place conduit between State and Calapooia, north	2 days	Wed 4/11/18	Thu 4/12/18	Kunert					
13	form curbs and sidewalk from State to Calapooia, north	2 days	Fri 4/13/18	Mon 4/16/18	Guido					

Project: CENTRAL AVE. SCHEDU
Date: Tue 3/27/18

7 14 21 28 Feb '18 4 11 18 25 Mar '18 4 11 18 25 Apr '18 1 8 15 22 29 May '18 6 13

Quality Fence

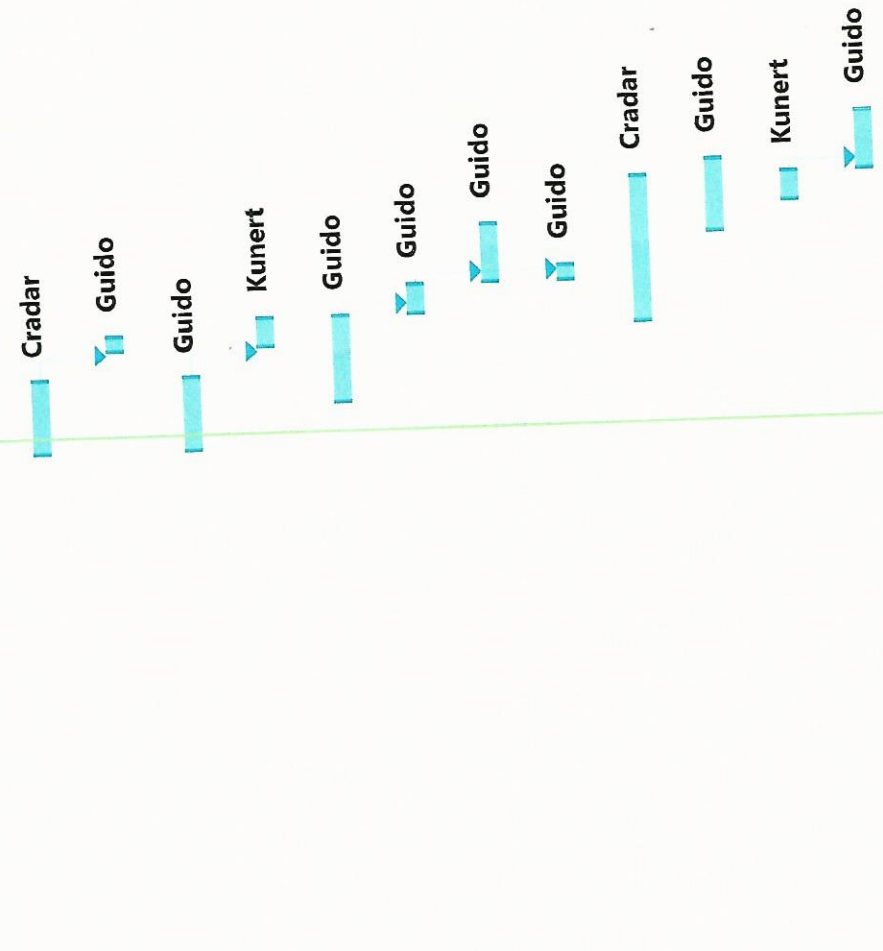

- Task
- Split
- Milestone
- Summary
- Project Summary
- Inactive Task
- Inactive Milestone
- Inactive Summary
- Manual Task
- Duration-only
- Manual Summary Rollup
- Manual Summary
- Start-only
- Finish-only
- External Tasks
- External Milestone
- Deadline
- Progress
- Manual Progress

Project: CENTRAL AVE. SCHEDU
Date: Tue 3/27/18
