


ID	Task Name	Duration	Start	Finish	Resource Names	Dec '17	Jan '18	Feb '18
1	Close west bound lane to traffic from Ash St to Comstock St.	21 days	Mon 1/8/18	Mon 2/5/18	Guido	3	7	11
2	Complete underground and demo work at Kruse St	4 days	Mon 1/8/18	Thu 1/11/18	Cradar			
3	Complete demo and sidewalk prep on south side of Central between Umpqua and	4 days	Mon 1/8/18	Thu 1/11/18	Guido			
4	Demo sidewalk and curb between Umpqua and State Streets.	6 days	Fri 1/12/18	Fri 1/19/18	Guido			
5	<New Task>							
6	Setup and pour back sidewalk and ramps between Umpqua and Williamette, south side	4 days	Wed 1/10/18	Mon 1/15/18	Guido			
7	Begin demo and underground at Branton St., north side.	6 days	Mon 1/8/18	Mon 1/15/18	Cradar			
8	Pour back ADA ramps, curbs and sidewalks between Umpqua and State St. Block out light pole bases for Kunert.	8 days	Fri 1/19/18	Tue 1/30/18	Guido			
9	Pour back ADA ramps at Branton Street, north side	3 days	Wed 1/10/18	Fri 1/12/18	Guido			
10	Setup and pour basin bottoms at Branton St., north	2 days	Mon 1/15/18	Tue 1/16/18	Guido			
11	Set up temp ped crossings for Grant Street to Comstock	8 days	Mon 1/15/18	Wed 1/24/18	Guido			
12	Begin demo and underground work on Robinson Street, north side.	6 days	Mon 1/15/18	Mon 1/22/18	Cradar			

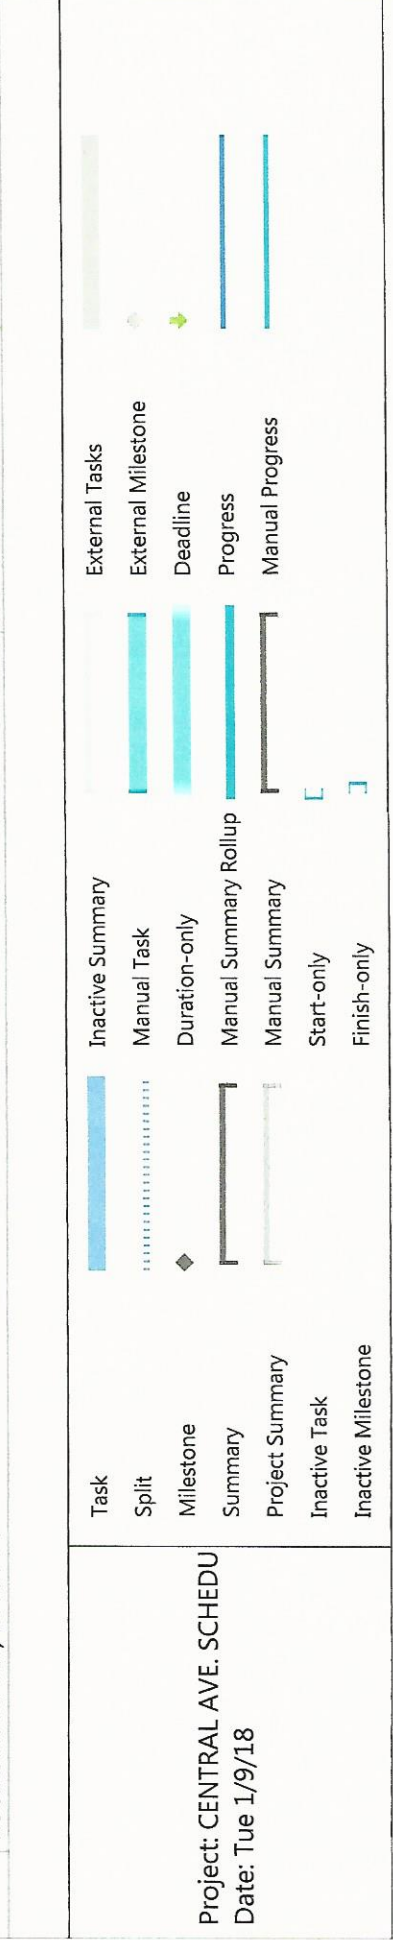

ID	Task Name	Duration	Start	Finish	Resource Names	Dec '17	Jan '18	Feb '18
13	Setup and pour ADA ramps at Kruse St. north	3 days	Fri 1/12/18	Tue 1/16/18	Guido	3	7	11
14	Setup and pour ADA ramps at Robinson St. north	3 days	Mon 1/22/18	Wed 1/24/18	Guido			
15	Begin demo and underground work at Sta 1285+00 Lt.	2 days	Tue 1/23/18	Wed 1/24/18	Cradar			
16	Complete CG3 inlet and sidewalk repair at Sta 1285+00 Lt.	3 days	Thu 1/25/18	Mon 1/29/18	Guido			
17	begin demo, underground work and sw prep at Sta 1284+25 Lt.	5 days	Thu 1/25/18	Wed 1/31/18	Cradar			

Project: CENTRAL AVE. SCHEDU
Date: Tue 1/9/18

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	
